


		Nombre	Duracion	Inicio	Terminado	Predecesores	Nombres del Recurso
1		Inicio	0 days	15/04/26, 8:00a.m.	15/04/26, 8:00a.m.		
2		Fase 1: ANALISIS Y DISE...	10 days	15/04/26, 8:00a.m.	25/04/26, 5:00p.m.	1	
3		Especificacion de requisitos	2 days	15/04/26, 8:00a.m.	16/04/26, 5:00p.m.		
4		Diagramas UML	1 day	17/04/26, 8:00a.m.	17/04/26, 5:00p.m.	3	
5		Modelo de datos	1 day	21/04/26, 8:00a.m.	21/04/26, 5:00p.m.	4	
6		Refinamiento de requisitos	4 days	17/04/26, 8:00a.m.	21/04/26, 5:00p.m.	3	
7		Validacion con stakeholders	4 days	22/04/26, 8:00a.m.	25/04/26, 5:00p.m.	6	
8		Fase 2: PLANIFICACION ...	11 days	27/04/26, 8:00a.m.	8/05/26, 5:00p.m.	2	
9		Configuracion de entorno ...	5 days	27/04/26, 8:00a.m.	1/05/26, 5:00p.m.	7	
10		Configuracion de base de ...	3 days	2/05/26, 8:00a.m.	5/05/26, 5:00p.m.	9	
11		Configuracion de herrami...	3 days	6/05/26, 8:00a.m.	8/05/26, 5:00p.m.	9;10	
12		Fase 3: DESARROLLO	84 days	9/05/26, 8:00a.m.	14/08/26, 5:00p.m.	8	
13		Modulo de usuarios	21 days	9/05/26, 8:00a.m.	2/06/26, 5:00p.m.		
14		Backend de autenticacion	7 days	9/05/26, 8:00a.m.	16/05/26, 5:00p.m.	10	
15		Gestion de usuarios	7 days	18/05/26, 8:00a.m.	25/05/26, 5:00p.m.	14	
16		Asignacion de roles	7 days	26/05/26, 8:00a.m.	2/06/26, 5:00p.m.	15	
17		Modulo de tickets	28 days	3/06/26, 8:00a.m.	4/07/26, 5:00p.m.	13	
18		Creacion de tickets	7 days	3/06/26, 8:00a.m.	10/06/26, 5:00p.m.	16	
19		Clasificacion y asignacion	14 days	11/06/26, 8:00a.m.	26/06/26, 5:00p.m.	18	
20		Gestion de estados	7 days	27/06/26, 8:00a.m.	4/07/26, 5:00p.m.	19	
21		Modulo de reportes y da...	21 days	6/07/26, 8:00a.m.	29/07/26, 5:00p.m.	17	
22		Dashboard usuario	7 days	6/07/26, 8:00a.m.	13/07/26, 5:00p.m.	20	
23		Dashboard tecnico	7 days	14/07/26, 8:00a.m.	21/07/26, 5:00p.m.	22	
24		Dashboard administrador	7 days	22/07/26, 8:00a.m.	29/07/26, 5:00p.m.	23	
25		Modulo de notificaciones	14 days	30/07/26, 8:00a.m.	14/08/26, 5:00p.m.	21	
26			56 days	15/08/26, 8:00a.m.	19/10/26, 5:00p.m.	12	
27		Integracion de modulos	14 days	15/08/26, 8:00a.m.	31/08/26, 5:00p.m.	13;17;21;25	
28		Pruebas unitarias	14 days	1/09/26, 8:00a.m.	16/09/26, 5:00p.m.	27	
29		Pruebas de integracion	14 days	17/09/26, 8:00a.m.	2/10/26, 5:00p.m.	28	
30		Pruebas de aceptacion	14 days	3/10/26, 8:00a.m.	19/10/26, 5:00p.m.	29	
31		Fase 5: DESPLIEGUE	21 days	20/10/26, 8:00a.m.	12/11/26, 5:00p.m.		
32		Preparacion de produccion	7 days	20/10/26, 8:00a.m.	27/10/26, 5:00p.m.	30	
33		Deployment	7 days	28/10/26, 8:00a.m.	4/11/26, 5:00p.m.	32	
34		Monitoreo post-lanzamiento	7 days	5/11/26, 8:00a.m.	12/11/26, 5:00p.m.	33	
35		Fin	0 days	12/11/26, 5:00p.m.	12/11/26, 5:00p.m.	31	

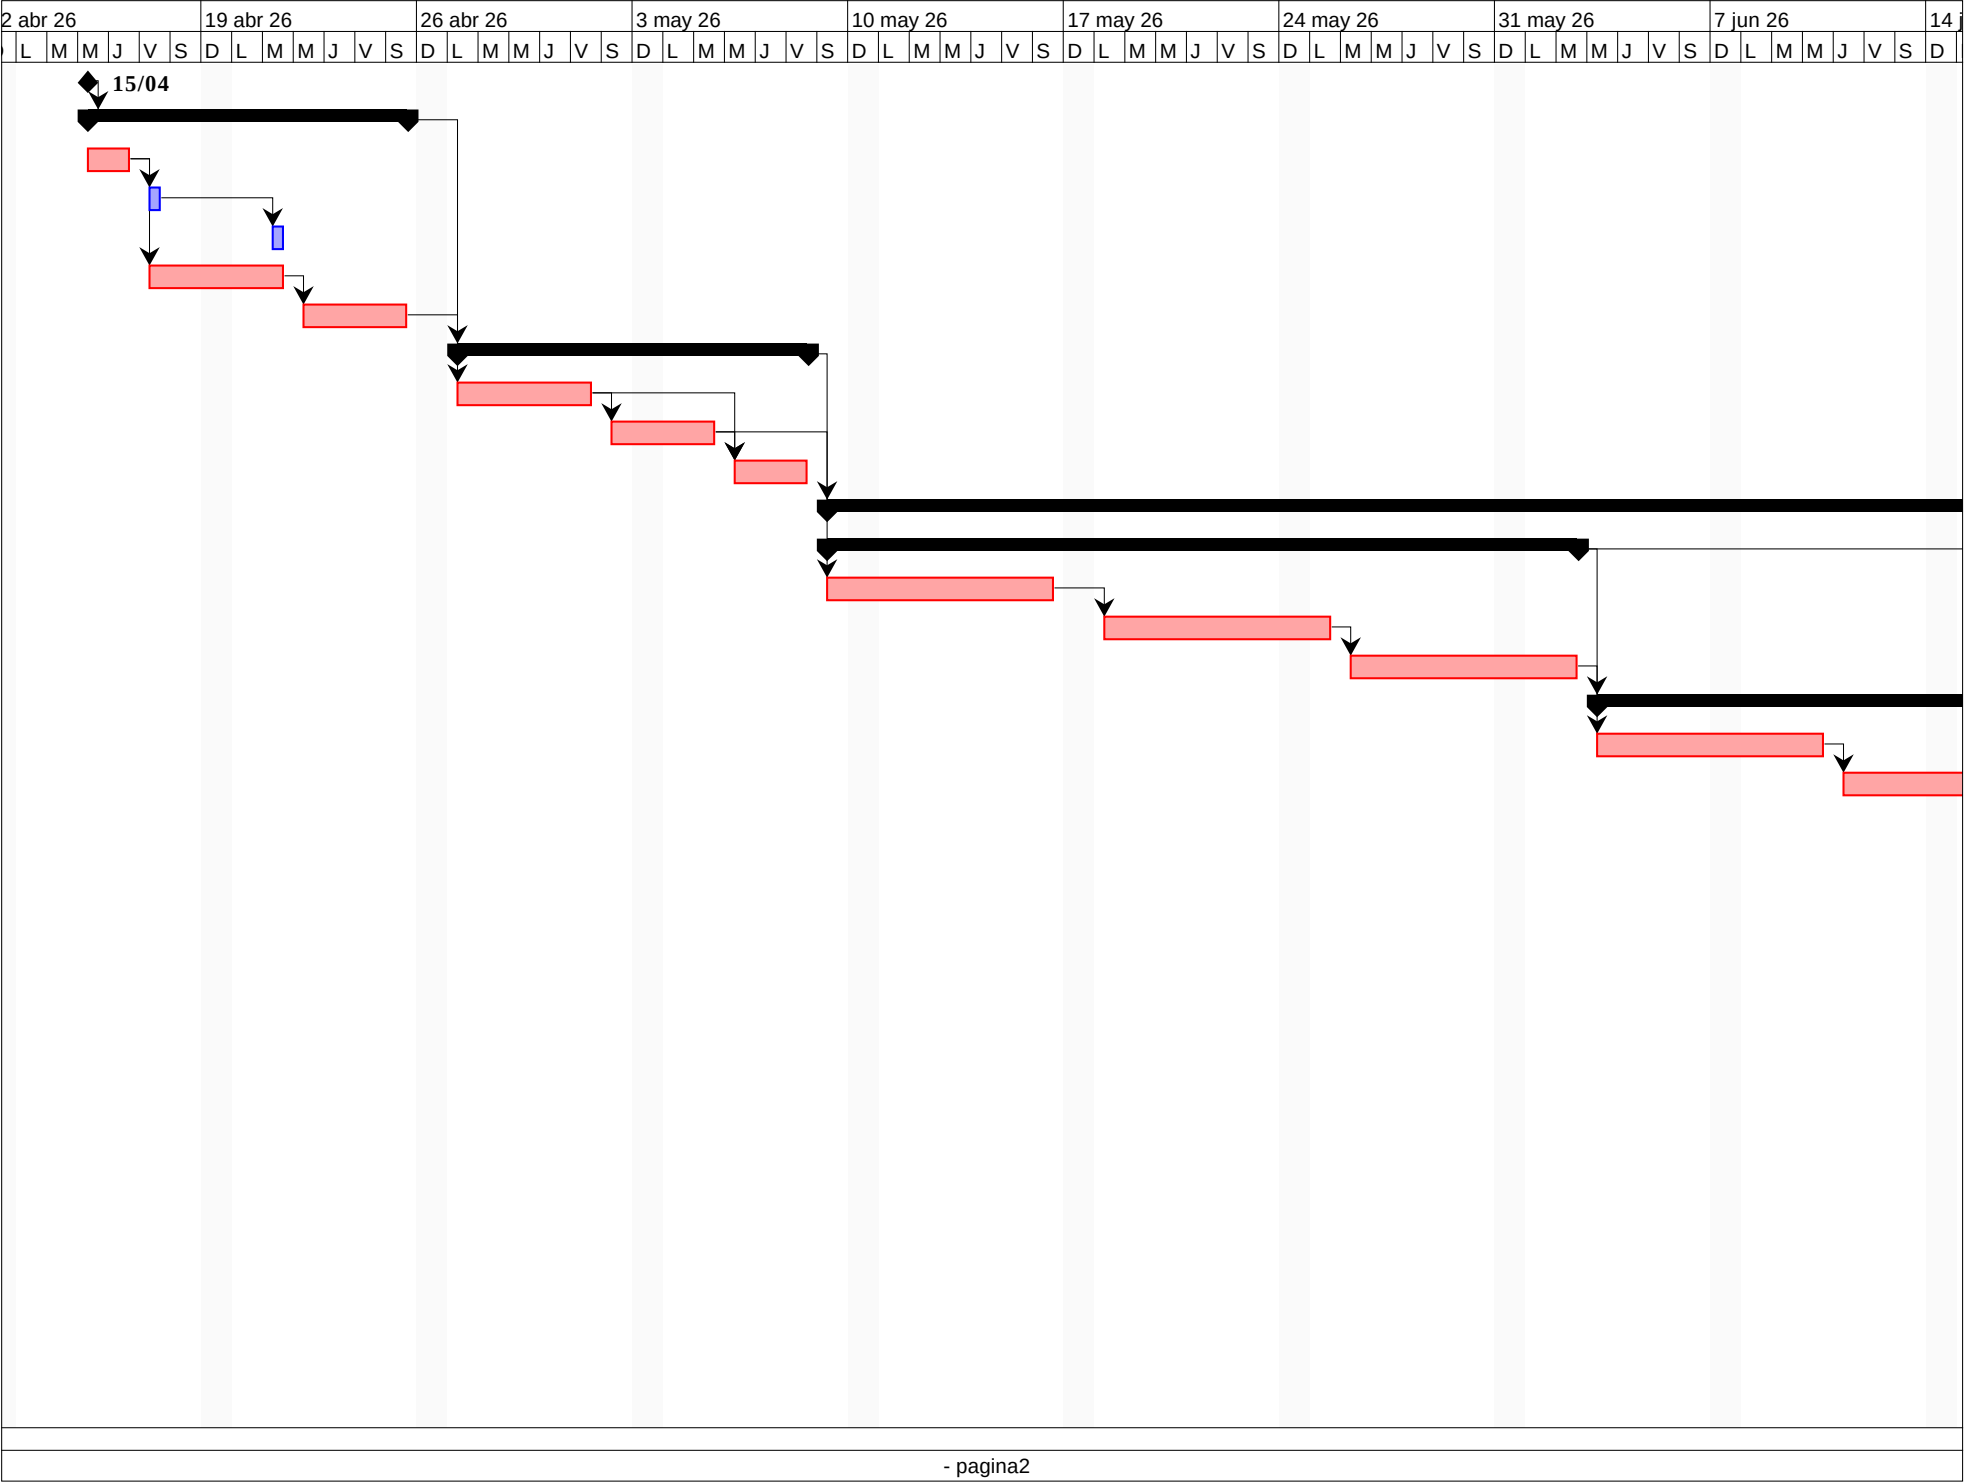

The Gantt chart displays a project schedule from June 21, 2026, to August 16, 2026. The timeline is marked with weekly intervals. The tasks and their durations are as follows:

- Task 1 (Black bar):** Starts on June 21, 2026, and ends on August 16, 2026.
- Task 2 (Black bar):** Starts on June 21, 2026, and ends on July 5, 2026.
- Task 3 (Red bar):** Starts on June 21, 2026, and ends on June 28, 2026.
- Task 4 (Red bar):** Starts on June 28, 2026, and ends on July 5, 2026.
- Task 5 (Black bar):** Starts on July 5, 2026, and ends on July 19, 2026.
- Task 6 (Red bar):** Starts on July 5, 2026, and ends on July 12, 2026.
- Task 7 (Red bar):** Starts on July 12, 2026, and ends on July 19, 2026.
- Task 8 (Red bar):** Starts on July 19, 2026, and ends on July 26, 2026.
- Task 9 (Red bar):** Starts on July 26, 2026, and ends on August 9, 2026.
- Task 10 (Black bar):** Starts on August 9, 2026, and ends on August 16, 2026.
- Task 11 (Red bar):** Starts on August 9, 2026, and ends on August 16, 2026.

Dependencies are indicated by arrows:

- Task 3 depends on Task 1.
- Task 4 depends on Task 2.
- Task 5 depends on Task 2.
- Task 6 depends on Task 5.
- Task 7 depends on Task 6.
- Task 8 depends on Task 7.
- Task 9 depends on Task 5.
- Task 10 depends on Task 9.
- Task 11 depends on Task 10.

o 26					23 ago 26					30 ago 26					6 sept 26					13 sept 26					20 sept 26					27 sept 26					4 oct 26					11 oct 26					18 oct 26				
M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M	M	J	V	S	D	L	M

